









PROJECT UPDATE

OCTOBER 2015



PROJECT A DUZINE -1- ROOF



NYSED APPROVED
BIDDING/REVIEW DEC -2015/JANUARY 2016
AWARD FEBRUARY 2016
CONSTRUCTION JULY-SEPTEMBER 2016
PROJECT CLOSED OUT JANUARY 2017



PROJECT B LENAPE/HS FOLDING WALL



AWARDED CONSTRUCTION

SECOND SHIFT
 DOORS MID TO LATE OCTOBER
 SUBSTANTIAL COMPLETION NOVEMBER 2015

 PROJECT CLOSED OUT FEBRUARY 2016



PROJECT C HS ROOF - PARKING LOT



DOCUMENTS SUBMITTED NYSED

DECEMBER 2015

NYSED -LEVEL 1 REVIEW APPROVAL

FEBRUARY 2016

ROOF WORK


BIDDING/REVIEW JAN/FEB 2016

AWARD MARCH 2016

CONSTRUCTION JULY-SEPTEMBER 2016

PROJECT CLOSED OUT JANUARY 2017





PROJECT C HS ROOF - PARKING LOT




SITE-PARKING LOT WORK

BIDDING/REVIEW JAN/FEB 2017 AWARD MARCH 2017 CONSTRUCTION JULY-SEPTEMBER 2017 PROJECT CLOSED OUT JANUARY 2018



PROJECT D MIDDLE SCHOOL ROOF



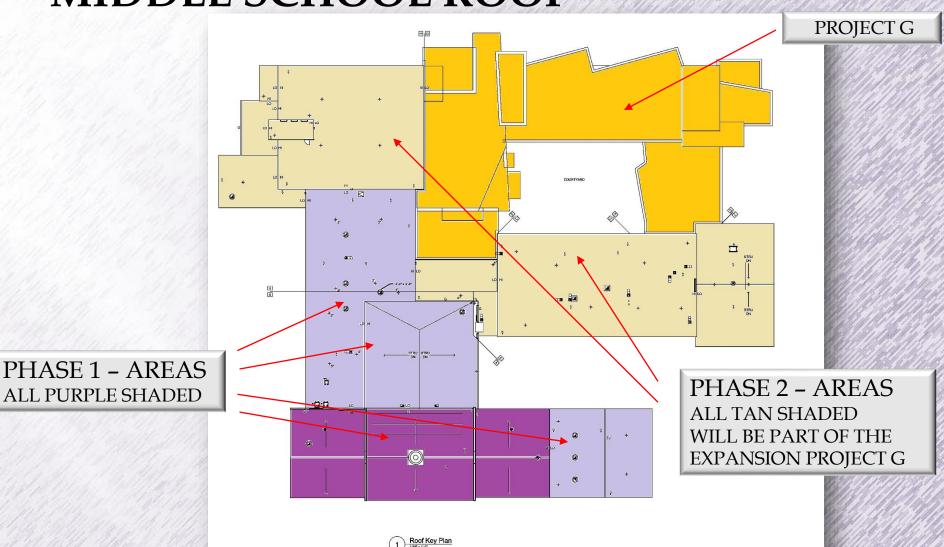

TETRATECH ARCHITECTS & ENGINEERS

the Palombo Group

PROJECT D MS ROOF - PHASE 1



DOCUMENTS SUBMITTED NYSED

DECEMBER 2015

NYSED -LEVEL 1 REVIEW APPROVAL

FEBRUARY 2016


BIDDING/REVIEW JAN/FEB 2016

AWARD MARCH 2016

CONSTRUCTION JULY-SEPTEMBER 2016

PROJECT CLOSED OUT JANUARY 2017





PROJECT E - PROJECTED NYSED APPROVAL SCENARIO I DUZINE-2 / LENAPE-2 BALANCE OF RENOVATIONS



DOCUMENTS SUBMITTED NYSED

■ MID OCTOBER 2015

NYSED -LEVEL 1 REVIEW APPROVAL

FEBRUARY 2016

BIDDING/REVIEW JAN/FEB 2016

AWARD MARCH 2016

CONSTRUCTION JULY-SEPTEMBER 2016

PROJECT CLOSED OUT JANUARY 2017



PROJECT E - PROJECTED NYSED APPROVAL SCENARIO II DUZINE-2 / LENAPE-2 BALANCE OF RENOVATIONS



DOCUMENTS SUBMITTED NYSED

MID OCTOBER 2015

NYSED -APPROVAL - AUGUST 2016 BIDDING/REVIEW JUNE/JULY 2016 AWARD AUGUST 2016 CONSTRUCTION

OCTOBER 2016 (second shift) JANUARY 2017
 PROJECT CLOSED OUT MARCH 2017



PROJECT F - PROJECTED NYSED APPROVAL SCENARIO I HIGH SCHOOL ADDITIONS/BALANCE OF WORK



DOCUMENTS SUBMITTED NYSED

■ MID NOVEMBER 2015

NYSED - APPROVAL - APRIL 2016


BIDDING/REVIEW MARCH/APRIL 2016

AWARD MAY 2016

CONSTRUCTION

- PHASE 1 ADDITION JULY DECEMBER 2016
- PHASE 2 RENOVATION JULY- SEPTEMBER 2016
- PHASE 3 GUIDANCE CONVERSION SUMMER 2017





PROJECT F HIGH SCHOOL - ADDITION







PROJECT F - PROJECTED NYSED APPROVAL SCENARIO II HIGH SCHOOL ADDITIONS/BALANCE OF WORK



DOCUMENTS SUBMITTED NYSED

■ MID NOVEMBER 2015

NYSED – APPROVAL – AUGUST 2016

BIDDING/REVIEW JUNE/JULY 2016

AWARD AUGUST 2016

CONSTRUCTION

- PHASE 1 ADDITION OCTOBER 16 MARCH 2017
- PHASE 2 RENOVATION SUMMER 2017
- PHASE 3 GUIDANCE CONVERSION SUMMER 2017



PROJECT F1 - PROJECTED NYSED APPROVAL SCENARIO I TRANSPORTATION ADDITION



DOCUMENTS SUBMITTED NYSED

JANUARY 2016

NYSED - APPROVAL - JUNE 2016

BIDDING/REVIEW MAY/JUNE 2016

AWARD JUNE 2016

CONSTRUCTION - AUG - DECEMBER 2016



PROJECT F1 - PROJECTED NYSED APPROVAL SCENARIO II TRANSPORTATION ADDITION



DOCUMENTS SUBMITTED NYSED

■ JANUARY 2016

NYSED – APPROVAL – OCTOBER 2016 BIDDING/REVIEW SEPT/ OCT 2016 AWARD OCTOBER 2016 CONSTRUCTION – SPRING 2017



PROJECT F2 TRANSPORTATION SEPTIC







PROJECT F2 TRANSPORTATION SEPTIC



DOCUMENTS SUBMITTED

- NYSDEC SEPTEMBER 21, 2015
- NYSED OCTOBER 1, 2015

APPROVAL

- NYSDEC ANTICIPATED NOVEMBER 2015
- NYSED LEVEL 1 NOVEMBER 2015

BIDDING - OCTOBER 2015

AWARD - NOVEMBER 2015

CONSTRUCTION - DECEMBER 2015



PROJECT H DISTRICT WIDE TECHNOLOGY



EXCEPT MIDDLE SCHOOL

DOCUMENTS SUBMITTED NYSED

MID DECEMBER 2015

NYSED - APPROVAL - APRIL 2016

BIDDING/REVIEW FEBRUARY/APRIL 2016

AWARD - APRIL 2016

CONSTRUCTION - JULY - DECEMBER 2016



MIDDLE SCHOOL ADDITIONS/RENOVATIONS OF WORK



PROJECT G - PROJECTED NYSED APPROVAL SCENARIO I MIDDLE SCHOOL ADDITIONS/RENOVATIONS OF WORK



DOCUMENTS SUBMITTED NYSED

MID DECEMBER 2015

NYSED – APPROVAL – MAY 2016 BIDDING/REVIEW APRIL/MAY 2016 AWARD JUNE 2016



PROJECT G - PROJECTED NYSED APPROVAL SCENARIO I MIDDLE SCHOOL ADDITIONS/RENOVATIONS OF WORK



CONSTRUCTION

- PHASE 1 ADDITION SEPT APRIL 2017
- PHASE 1 RENOVATION JULY- APRIL 2017
- PHASE 2 RENOVATION APR SEPT 2017
- PHASE 2 SPACE CONFIGURATION JULY/SEPT 17
- PHASE 3 RENOVATION JUNE 2018 SEPT 18



PROJECT G - PROJECTED NYSED APPROVAL SCENARIO II MIDDLE SCHOOL ADDITIONS/RENOVATIONS OF WORK



DOCUMENTS SUBMITTED NYSED

MID DECEMBER 2015

NYSED – APPROVAL – SEPTEMBER 2016 BIDDING/REVIEW JULY/AUG 2016 AWARD SEPTEMBER 2016



PROJECT G - PROJECTED NYSED APPROVAL SCENARIO II MIDDLE SCHOOL ADDITIONS/RENOVATIONS OF WORK



CONSTRUCTION

- PHASE 1 ADDITION OCT JULY 2017
- PHASE 1 RENOVATION JULY- APRIL 2017
- PHASE 2 RENOVATION APR SEPT 2017
- PHASE 2 SPACE CONFIGURATION JULY/SEPT 17
- PHASE 3 RENOVATION JUNE 2018 DEC 18



SOUTH ENTRY - BUS DROP OF SIDE







BIRDSEYE - LOOKING NORTH





BIRDSEYE - LOOKING WEST








"GUNKS" TEXTURE- ALTERNATE



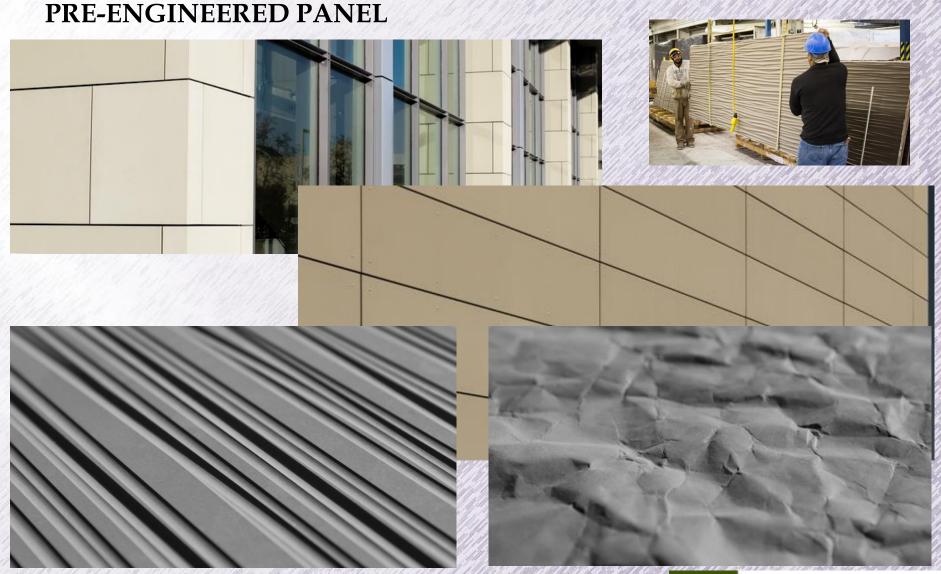



COURTYARD - LOOKING NORTH



BASE BID



COURTYARD - LOOKING EAST

ALTERNATE BID - COURTYARD DESIGN





COURTYARD - LOOKING NORTH

ALTERNATE BID - COURTYARD DESIGN





COURTYARD - LOOKING SOUTH

ALTERNATE BID - COURTYARD DESIGN







NORTH ENTRY - MAIN/DROP OFF







NORTH ENTRY - MAIN / DROP OFF















