



## CONSTRUCTION UPDATE TO THE BOARD OF EDUCATION SEPTEMBER 2017

NEW PALTZ CENTRAL SCHOOL DISTRICT: PROJECTS E, F, & G



#### **PROJECT TEAM**









DISTRIBUTION LIST: Michael O'Donnell, Alison Easton, Brian Cournoyer, Kathy Preston, Sophia Skiles, Teresa Thompson, Matthew Williams, Maria Rice, Rick Linden, Stephen Callahan, Dusti Callo, Tetra Tech, The Palombo Group









## AGENDA



### **SUMMARY**

- I. REVIEW PROJECT STRUCTURE AND STATUS
- II. REVIEW INDIVIDUAL BUILDINGS AND ASSOCIATED CONSTRUCTION



### **PHASES**

- DUZINE ES
- LENAPE ES
- MIDDLE SCHOOL
- HIGH SCHOOL



### III. SAFETY









### I. SUMMARY OF PROJECTS AND STATUS



Project A - Duzine Roof Completed August 2016

Project B – Lenape - HS Wall Completed

• Project C - HS - Roof Completed August 2016

Project C - HS - Site
Refurbish parking and circulation, to be bid for Summer 2018

Completed August 2016

Project D - MS Roof

Project E – Len. / Duz. Renos

Awarded / Currently Under Construction – E.T.C. Aug. 2017

Project F – HS – Adds / Renos Awarded

Awarded / Currently Under Construction – E.T.C. Nov. 2017

Project F1 - Bus Adds

Documents submitted to NYSED / awaiting approvals

Project F2 - Bus Garage Septic Completed

• Project G - MS Adds / Renos Awarded / Currently Under Construction – E.T.C. Fall 2019

• **Project H - District Wide Tech** Awarded / Currently Under Construction – E.T.C. Fall 2017













II. DUZINE ES





### **Current Scopes of work being performed:**


### **Program Improvements – Summer 2017**

- Add gang bathrooms near the cafeteria.
- Update network infrastructure to support current and future technologies

### **Infrastructure Improvements – Summer 2017**

- Replace damaged doors at the Cafeteria and Gymnasium, including safety glass
- Preserve building exterior and prevent leaks by replacing cracked bricks
- Upgrade antiquated clock and public address (PA) system
- Replace obsolete electrical panels
- Add ventilation in corridors to meet code and improve health














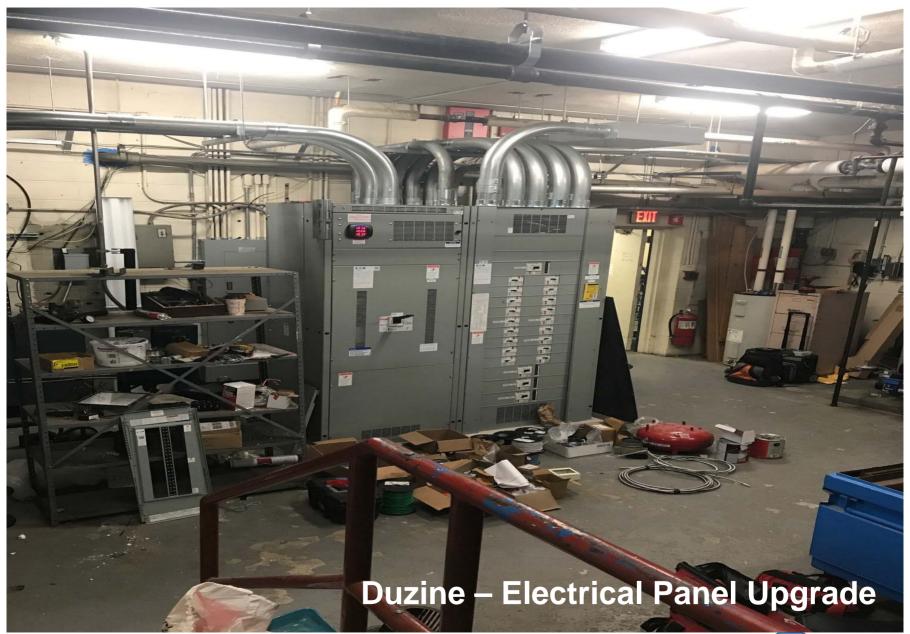





II. LENAPE ES





### **Current Scopes of work being performed:**

### **Program Improvements - Summer 2017**

- Provide additional storage space
- Update network infrastructure to support current and future technologies

### **Infrastructure Improvements – Summer 2017**

- Address leaking exterior walls
- Upgrade all HVAC controls not included in the previous Energy Performance Contract
- Upgrade fire alarm and smoke detection system
- Add ventilation in various areas to improve air quality















# II. NEW PALTZ MIDDLE SCHOOL





### **Current Scopes of work being performed:**

### **Program Improvements – School Year 2017 / 2018/ 2019**

- 35,000 Square Foot Classroom Addition
- Classroom Renovations throughout the existing building
- Update network infrastructure to support current and future technologies



### Infrastructure Improvements – School Year 2017 / 2018/ 2019

- Preserve building exterior / window replacements and brick re-pointing as needed
- Upgrade antiquated clock and public address (PA) system
- Replace obsolete electrical panels
- Add ventilation in corridors to meet code and improve health



### **Infrastructure Improvements – Summer 2017**

- New and improved site traffic circulation

















## II. NEW PALTZ HIGH SCHOOL





### **Current Scopes of work being performed:**

## **Program Improvements – Summer 2017**

- New 5 Classroom addition.



### **Program Improvements – Fall 2017**

- New Guidance Suite
- Conference Room renovations

## **Infrastructure Improvements – Summer 2017**


- Preserve building exterior / EIFIS work and scraping and painting exterior lintels
- Replace obsolete electrical panels
- Add controls and ventilation in areas to meet code and improve health










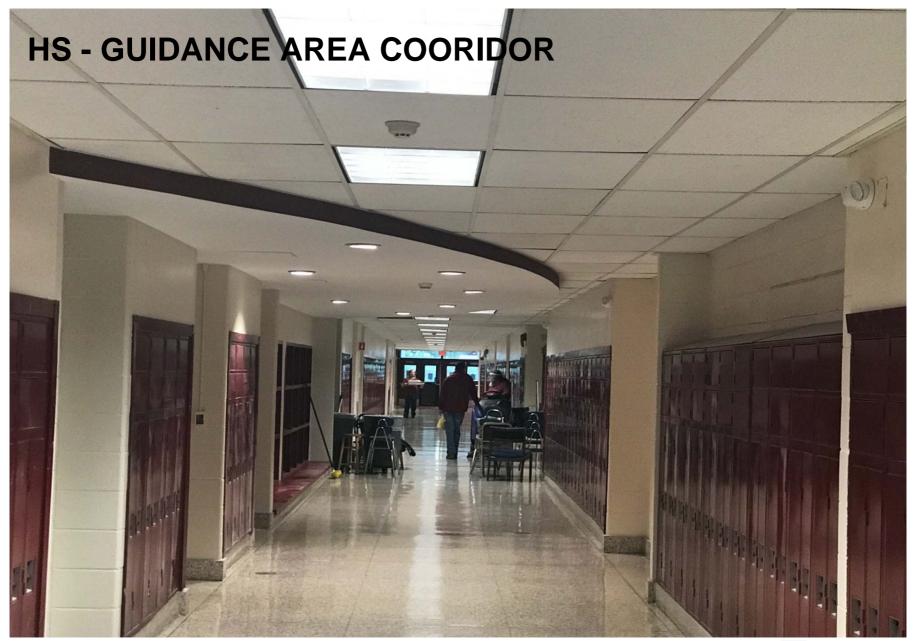

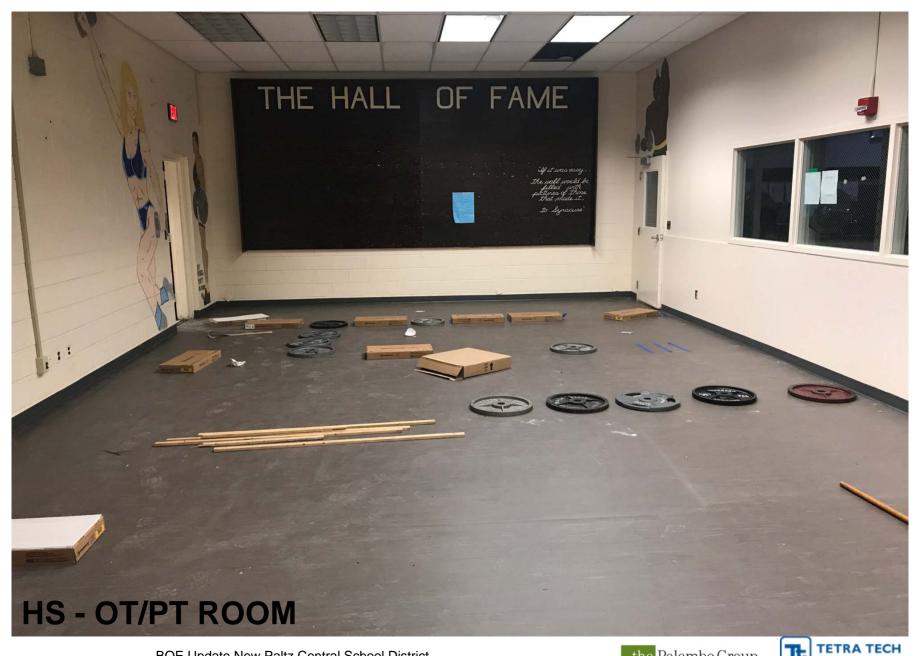









### SAFETY



STUDENT AND STAFF SAFETY IS OUR NUMBER ONE CONCERN.



PLEASE NOTIFY THE BUILDING PRINCIPAL OF ANY CONSTRUCTION SAFETY ISSUES SO THEY CAN BE ADDRESSED IMMEDIATELY. THE PRINCIPAL WILL THEN CONTACT THE PALOMOBO GROUP.



THANK YOU.

















